Haringey Civic Centre

Newsletter - Issue 08
November 2025

Our Team



Harry Nahum
Project Director
harrynahum@sisk.co.uk



Steve Eldergill
Senior Project Manager
steveeldergill@sisk.co.uk



Conor Moynihan
Senior Engineer
c.moynihan@sisk.co.uk



Abishek Ramachandra
Site Engineer
abhishekramachandra@sisk.co.uk

Works Update

- The concrete for the final level of the annexe building is being poured in 2 sections. It is expected that the final pour to the roof will be completed in November
- Level 2, the roof, of the link building has been poured thus concluding the concrete frame works for the link building
- The substation construction works on the Bounds Green Road side have been completed
- New lift shaft structural openings are being progressed for the Civic building which will facilitate the services installation



Link building Level 2, roof, pour complete



Annexe Level 3, roof and plant area, concrete pour 1

Works Update (continued)




Above: New lift shafts on Level 3 and 4 of the Civic Building

- The facade works have commenced on the ground floor of the annexe building. This involves the installation of a steel framing system (SFS) which will act as an envelope covering the building. Once complete the facade will provide weatherproofing, heat insulation and structural integrity to the new building
- The scaffold erection has continued to the main chamber which will allow workers to safely reach all parts of the walls and ceiling to complete connections and eventually aesthetic works



Above: Steel framing system (SFS) being erected on the ground floor of the annexe

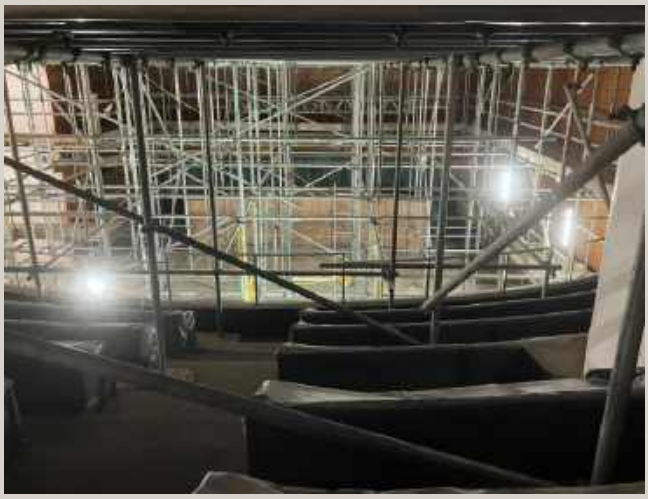

Above: Internal scaffolding being erected in the main chamber of the Civic Centre

- The final attenuation tank to help with drainage around the site has been installed

Upcoming works

The following works will be happening at the Civic Centre site through the end of November and December.


Some of the works will be visible from the streets around the Civic Centre but the majority of works will be internal.

ANNEXE

- Steel framing system facade works will be ongoing
- The final concrete pour of the main building will mark a significant milestone for the project. This is known as topping out which celebrates the point that the building being constructed reaches its maximum height

EXISTING CIVIC CENTRE BUILDING

- The lift shaft opening for the ground floor and level 1 of the Civic building needs to be completed. The lift shafts for levels 2, 3, 4 and the basement have already been installed
- New drainage runs are continuing to be installed around the existing Civic Centre
- New upstands are to be poured to facilitate the facade installation for the main Civic building
- Soffit remedial / repair works will be ongoing, which will improve fire safety and durability or the concrete slab when the building is completed
- Electrical and plumbing works will commence on level 3

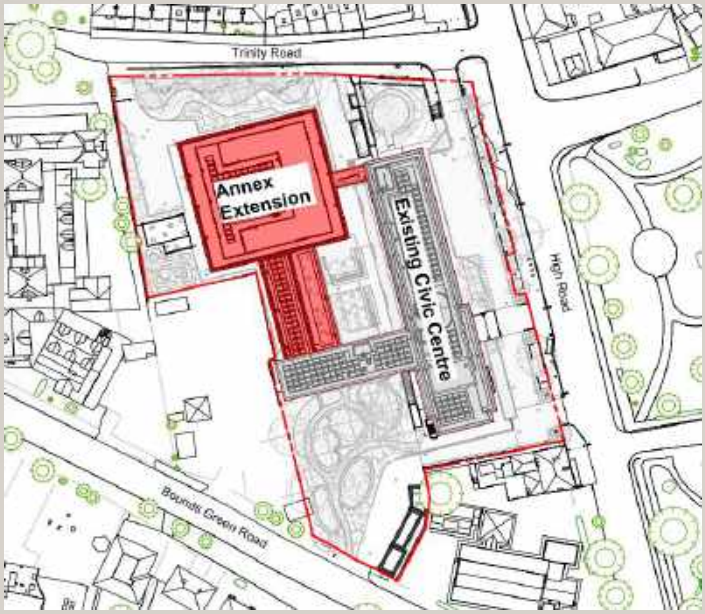

Community Liaison and Social Value

Sisk recently supported at the Careers and Innovations fair at the Tottenham Centre. Over 300 local people and students from Capital City College attended to hear about job and apprentice opportunities across an assortment of industries including construction.



Advice was offered on career paths and work placements with the trades working at the Civic Centre.

Three Haringey residents have recently started their construction industry path with carpentry apprenticeships.

Keep an eye on the Haringey Works pages for all the upcoming job and apprentice opportunities with us at. (**https://works.haringey.gov.uk**).

We want to be good neighbours whilst we are working in your community.

Please let us know of any ways that we can help you by contacting us at:

civicconstruction@sisk.co.uk

We have been capturing time lapse videos of the project progression which you can see every month through the Haringey Civic Centre website or through scanning the QR code below

Site working hours: 8am to 6pm on Monday - Friday
8am to 1pm on Saturday

Emergency Contacts

In case of Emergency please contact:
Steve Eldergill | 07385 557359
Harry Nahum | 07791 152412

More information about the project can be found at https://haringeyciviccentre.commonplace.is/ or by scanning the QR code
