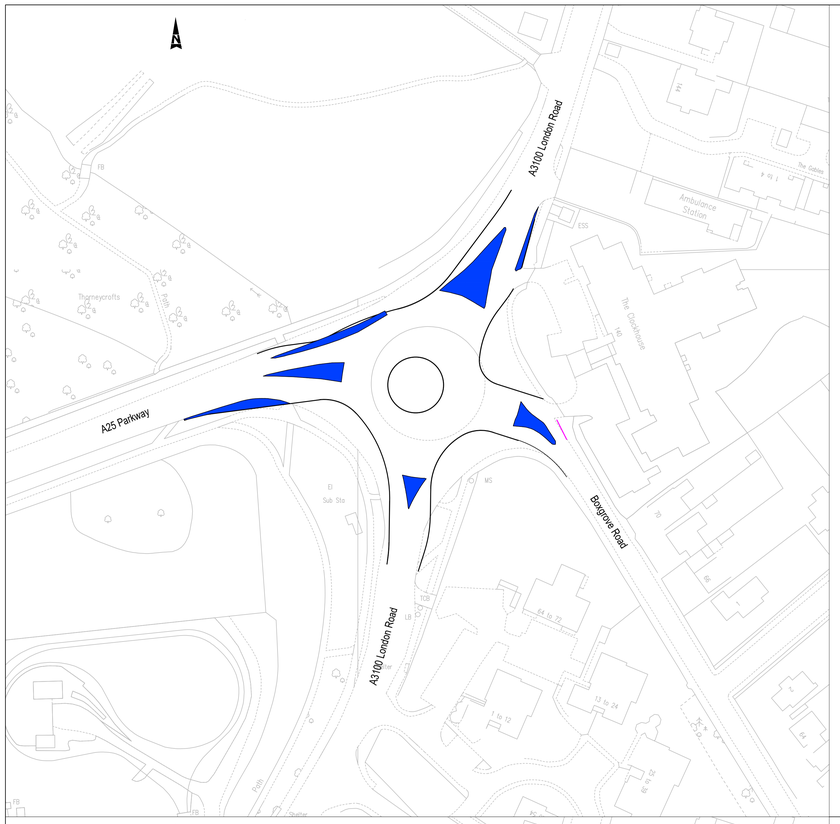


Phase 1- Reduce Roundabout Size and remove splitter islands


Description of Works

.
Change Kerb Inlets to Gullies (Night)
Binder Surfacing to fall to old gullies.
Widen NE and SW carriageways.
Traffic Management

Duration 4 Weeks

Daytime: Junction fully Functioning

Nightime (8pm to 5am): Lane Closures and 4 Way Lights

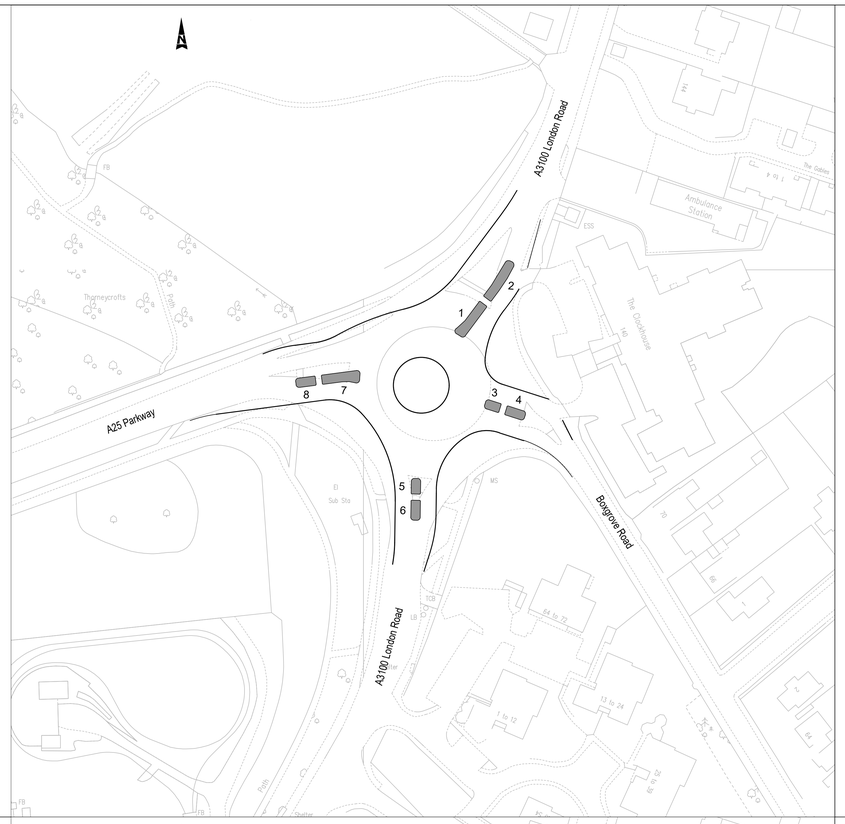

Phase 2 - Build 8 new splitter Islands

Description of Works


Construct Islands 1, 3, 5 and 7 first, followed by islands 2, 4, 6 and 8

Traffic Management

Duration: 3Weeks

Daytime: Junction fully Functioning

Nightime (8pm to 5am): Lane Closures and 4 Way Lights

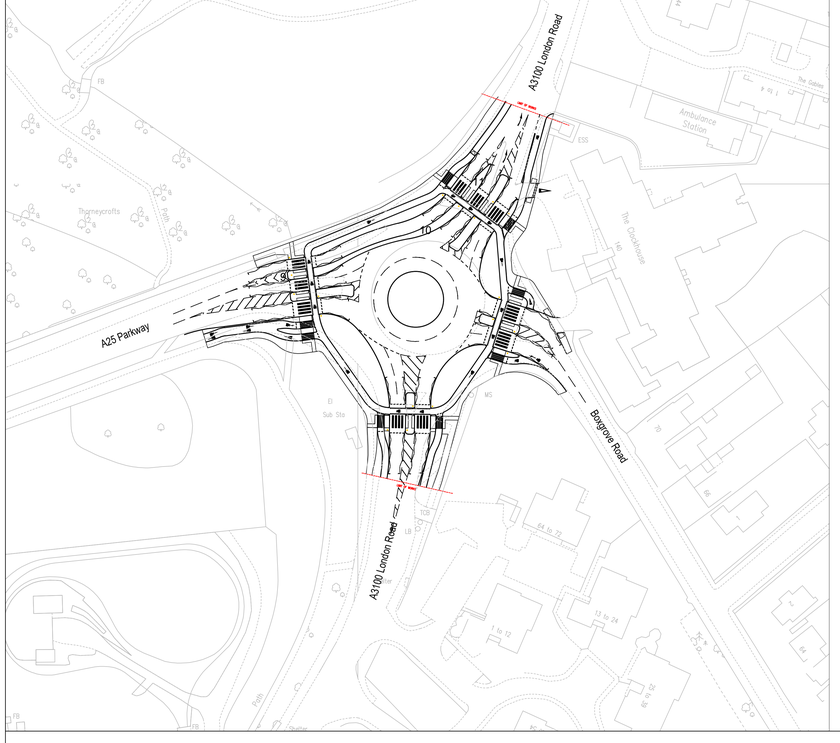

Phase 3 - Build NE, SE,SW Carriageway Edges and 3 Islands

Description of Works


Lay carriageway kerbs NE, SE and SW. Extend drainage (Nights and off peak).
Construct Islands 9, 10 and 11 (4 way lights. Nights for carriageway kerb edge. Days and Peak for off carriageway works).

Traffic Management

Duration 6 Weeks

Daytime: Junction fully Functioning

Nightime (8pm to 5am): Lane Closures and 4 Way Lights

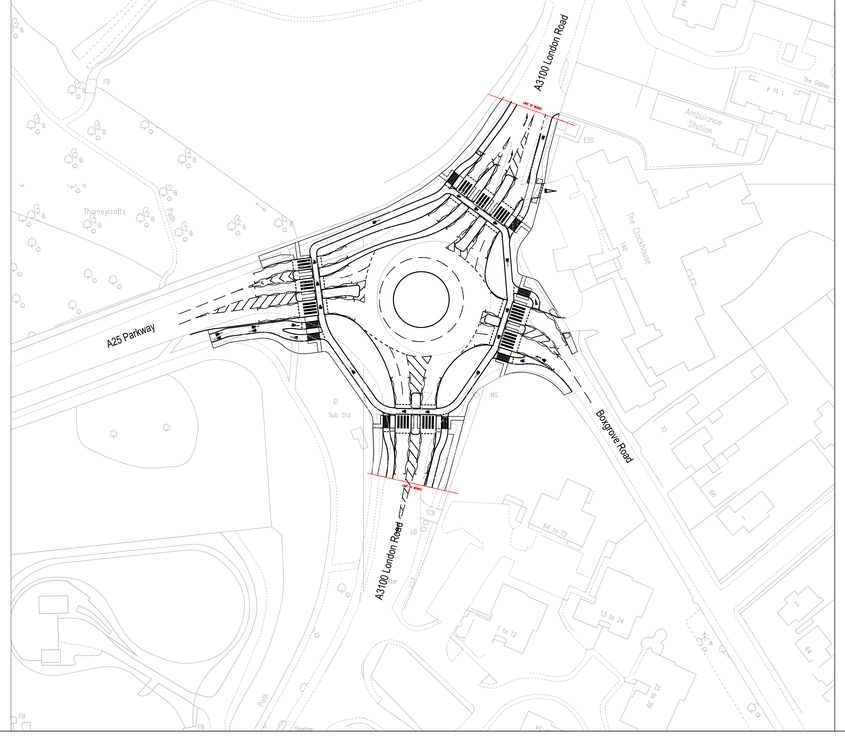

Phase 4 - Build NW Slip lane, footway and cycleways in NE, NW, SW and SE verge

Description of Works

Lay carriageway kerbs and extend drainage NW (Nights and off peak).
Resurface carriageway to new levels, lines and markings (Nights).
Build footway and cycleways off carriageway NE, NW, SE and SW (Days).

Traffic Management

Duration 8 Weeks

Daytime: Junction fully Functioning

Nightime (8pm to 5am): Slip lane closed and 4 Way Lights

BOXGROVE ROUNDABOUT
Traffic management
Proposals
