Haringey Civic Centre

Newsletter - Issue 07
October 2025

Our Team



Harry Nahum
Project Director
harrynahum@sisk.co.uk



Steve Eldergill
Senior Project Manager
steveeldergill@sisk.co.uk



Conor Moynihan
Senior Engineer
c.moynihan@sisk.co.uk



Abishek Ramachandra
Site Engineer
abhishekramachandra@sisk.co.uk

Works Update

- The scaffolding works have reached the final phase and are currently being erected around the west wing (Committee Rooms) section of the Civic Centre building.
- The new substation roof has now been completed with the doors currently being installed.
- Internal demolition works to the basement and upper floors of the Civic Centre have continued.
- A temporary mould called formwork is being erected in the link which connects the annex to the main Civic Centre building. This is used to support concrete when it is first poured until it has dried sufficiently and is then hard enough to support itself.



Completed roof on the new substation close to Bounds Green Road



Annex Level 2 concrete pour

Works Update (continued)



Above: Formwork being erected for the level 1 slab pour for the link building



Above: Stair/lift core wall on Level 1 poured

- The core structure of the annex building is now complete on the 1st floor (as above).





Above: new lift shafts on the first floor annex

Left: newly installed hoist

- The hoist to aid in moving materials and machines has been installed in the main Civic Centre building.
- Works to the new annex building have progressed to Level 2. Part of the concrete slab has been poured and once this is ready then the other half will be poured.

SISK ESTD. 1959
Improving the image of construction
Haringey LONDON

Upcoming works

The following works will be happening at the Civic Centre site through October and November.

Some of the works will be visible from the streets around the Civic Centre but the majority of works will be internal.


ANNEX

- Works will continue on from last month for the first floor slab (concrete flooring).

EXISTING CIVIC CENTRE BUILDING

- The new lift shaft for the Civic Centre building will be constructed and completed by the end of October.
- Internal demolition works to remove walls to reflect the new layout will continue.
- New drainage runs are continuing to be installed around the existing Civic Centre.
- Attenuation Tank 3 will be installed. This will mark the completion of all the tanks needed for the surface water drainage (to reduce the risk of excessive rainfall causing any flooding issues to the site and surrounding properties) around the Civic Centre site.



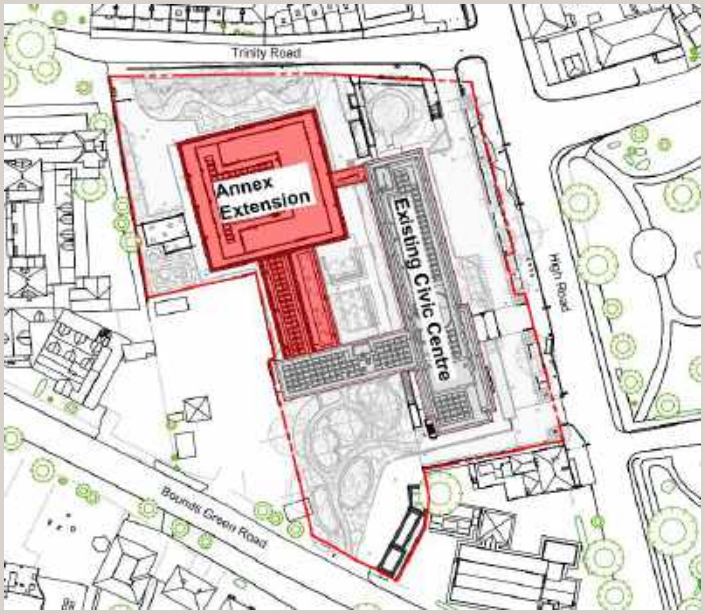

Above left: location of the surface water attenuation tanks with no 3 the final tank to be installed

SISK ESTD. 1959
Improving the image of construction
Haringey LONDON

Community Liaison and Social Value

An opportunity to become a **Stonemasonry apprentice** is currently live on the Haringey Works pages. (**https://works.haringey.gov.uk**).

Keep an eye on these pages for upcoming opportunities in **carpentry** and **labouring**.

If anyone has any questions about what is happening on site, or are interested in finding out more about a career in construction, then please feel free to reach out to us at the project email address and we would be happy to have an informal chat with you.

Alternatively **www.goconstruct.org** is a useful website with detailed information about the type of career you could pursue, with the skills or qualifications needed. There may well be something that you hadn't even considered.

We want to be good neighbours whilst we are working in your community.

Please let us know of any ways that we can help you by contacting us at:

civicconstruction@sisk.co.uk

We have been capturing time lapse videos of the project progression which you will soon be able to see every month through the Haringey Civic Centre website or through scanning the QR code below

Site working hours: 8am to 6pm on Monday - Friday
8am to 1pm on Saturday

Emergency Contacts

In case of Emergency please contact:
Steve Eldergill | 07385 557359
Harry Nahum | 07791 152412

More information about the project can be found at https://haringeyciviccentre.commonplace.is/ or by scanning the QR code
