

A3100 London Road Active Travel Schemes

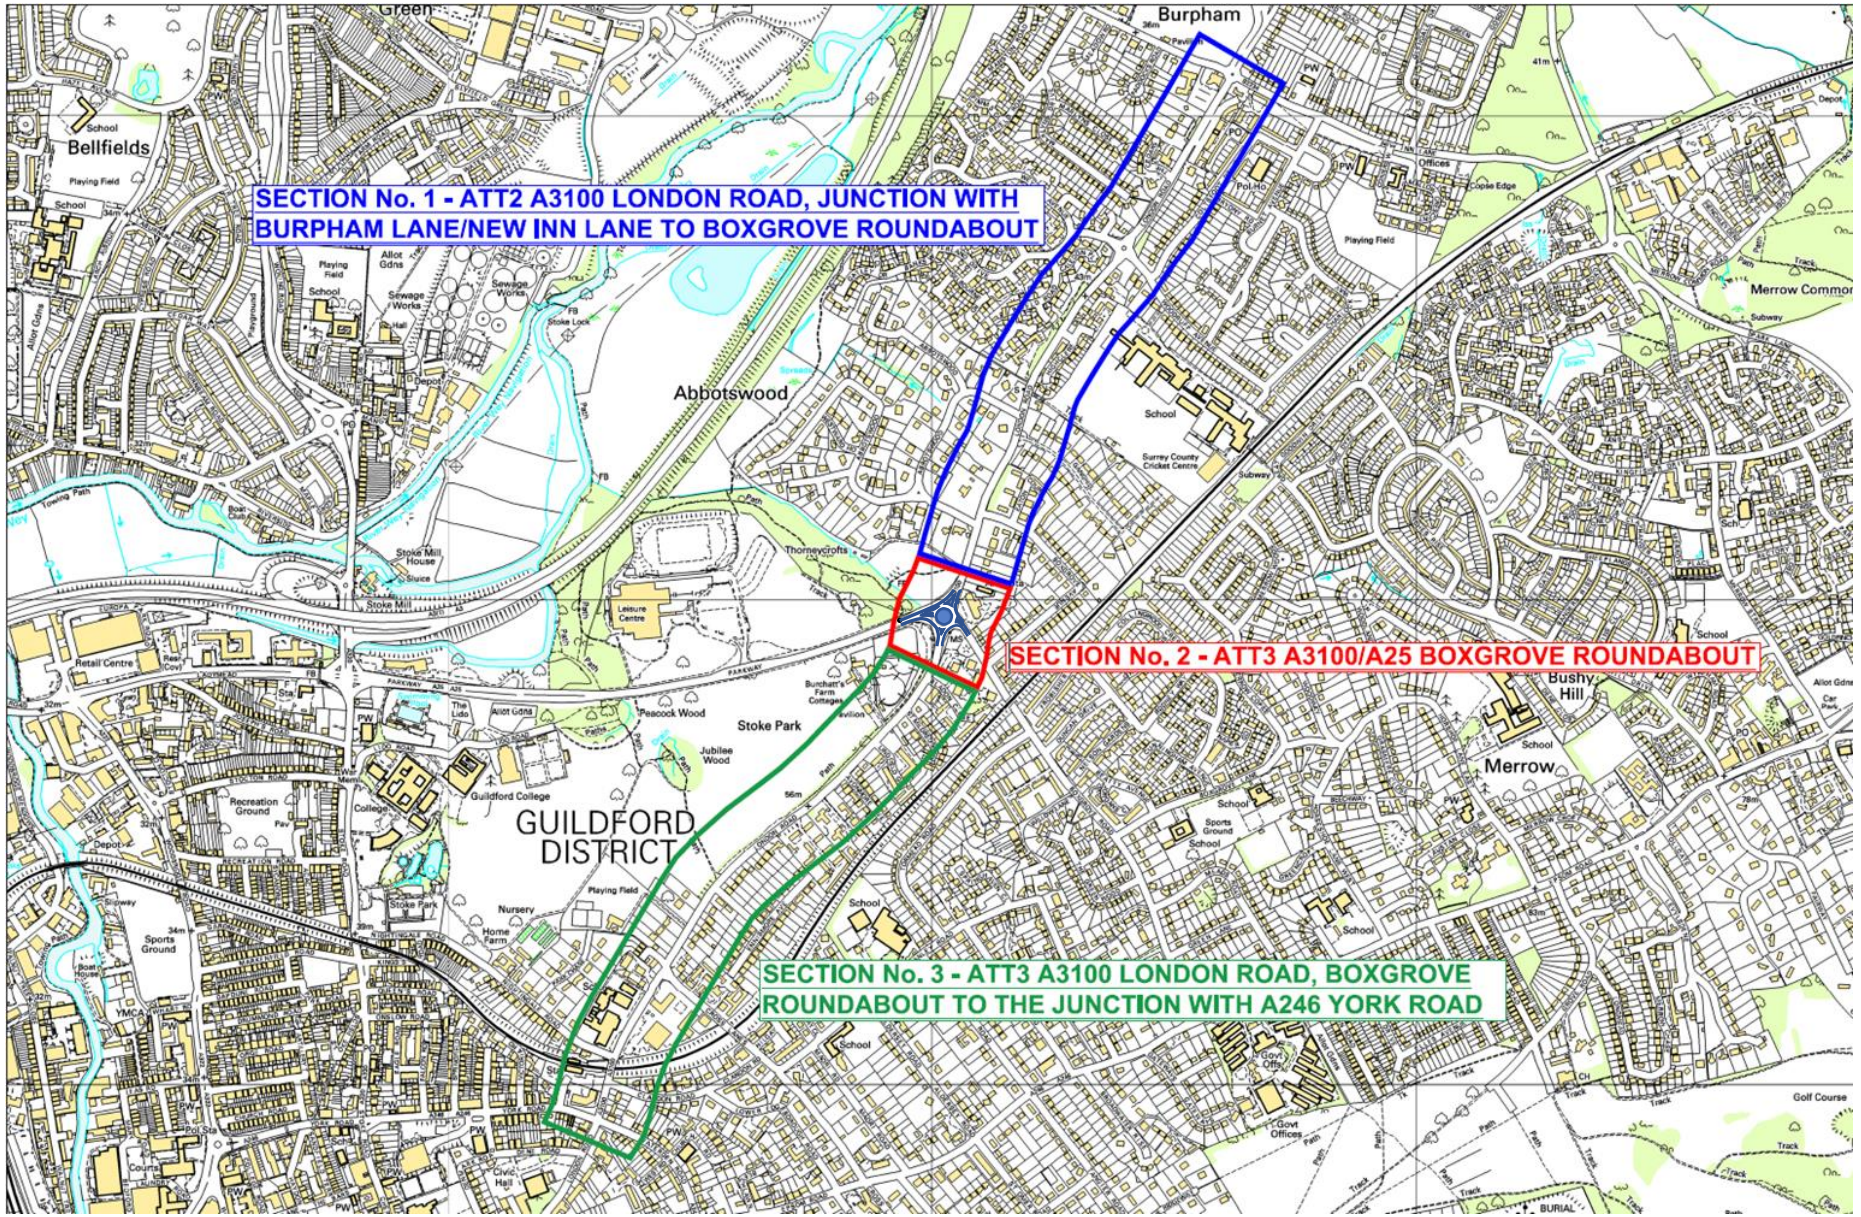


SECTION 2

BOXGROVE ROUNDABOUT

TRAFFIC MANGEMENT

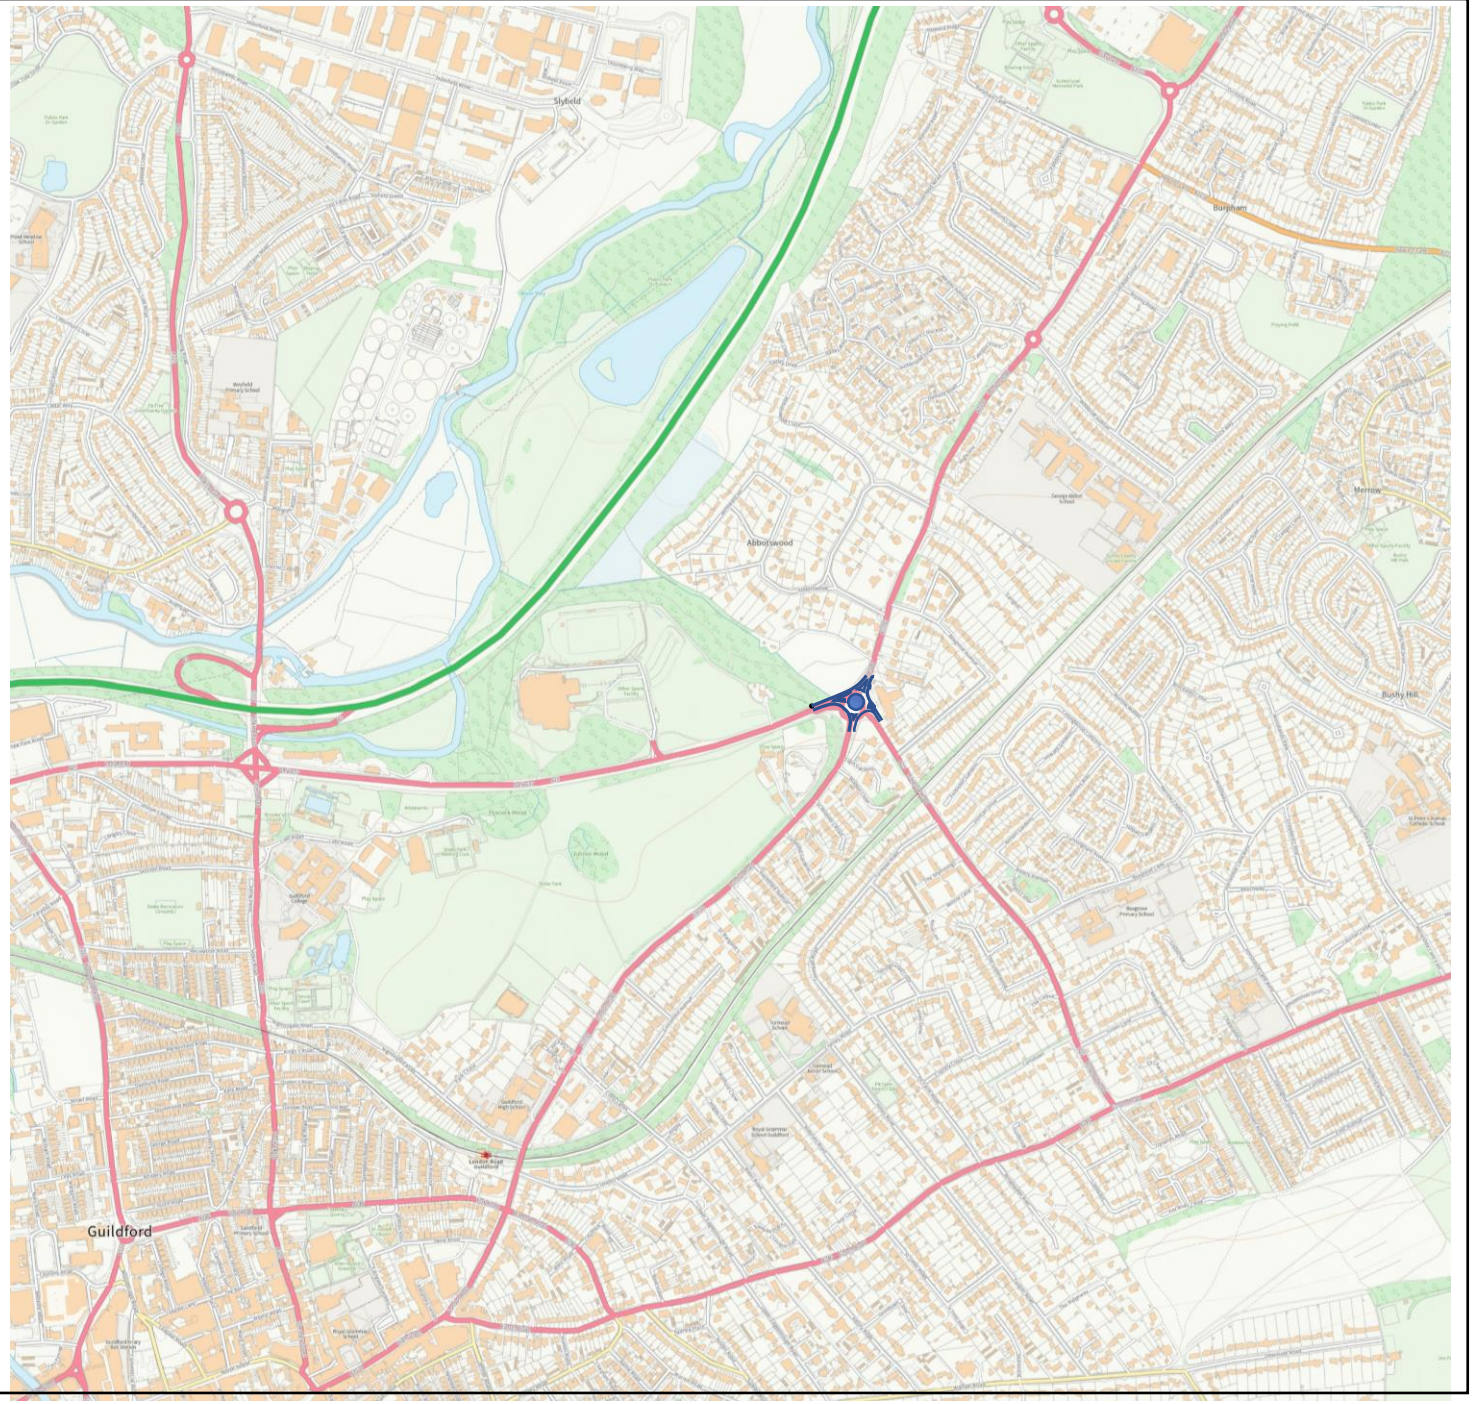

Phase 1 Programme (4 wks):

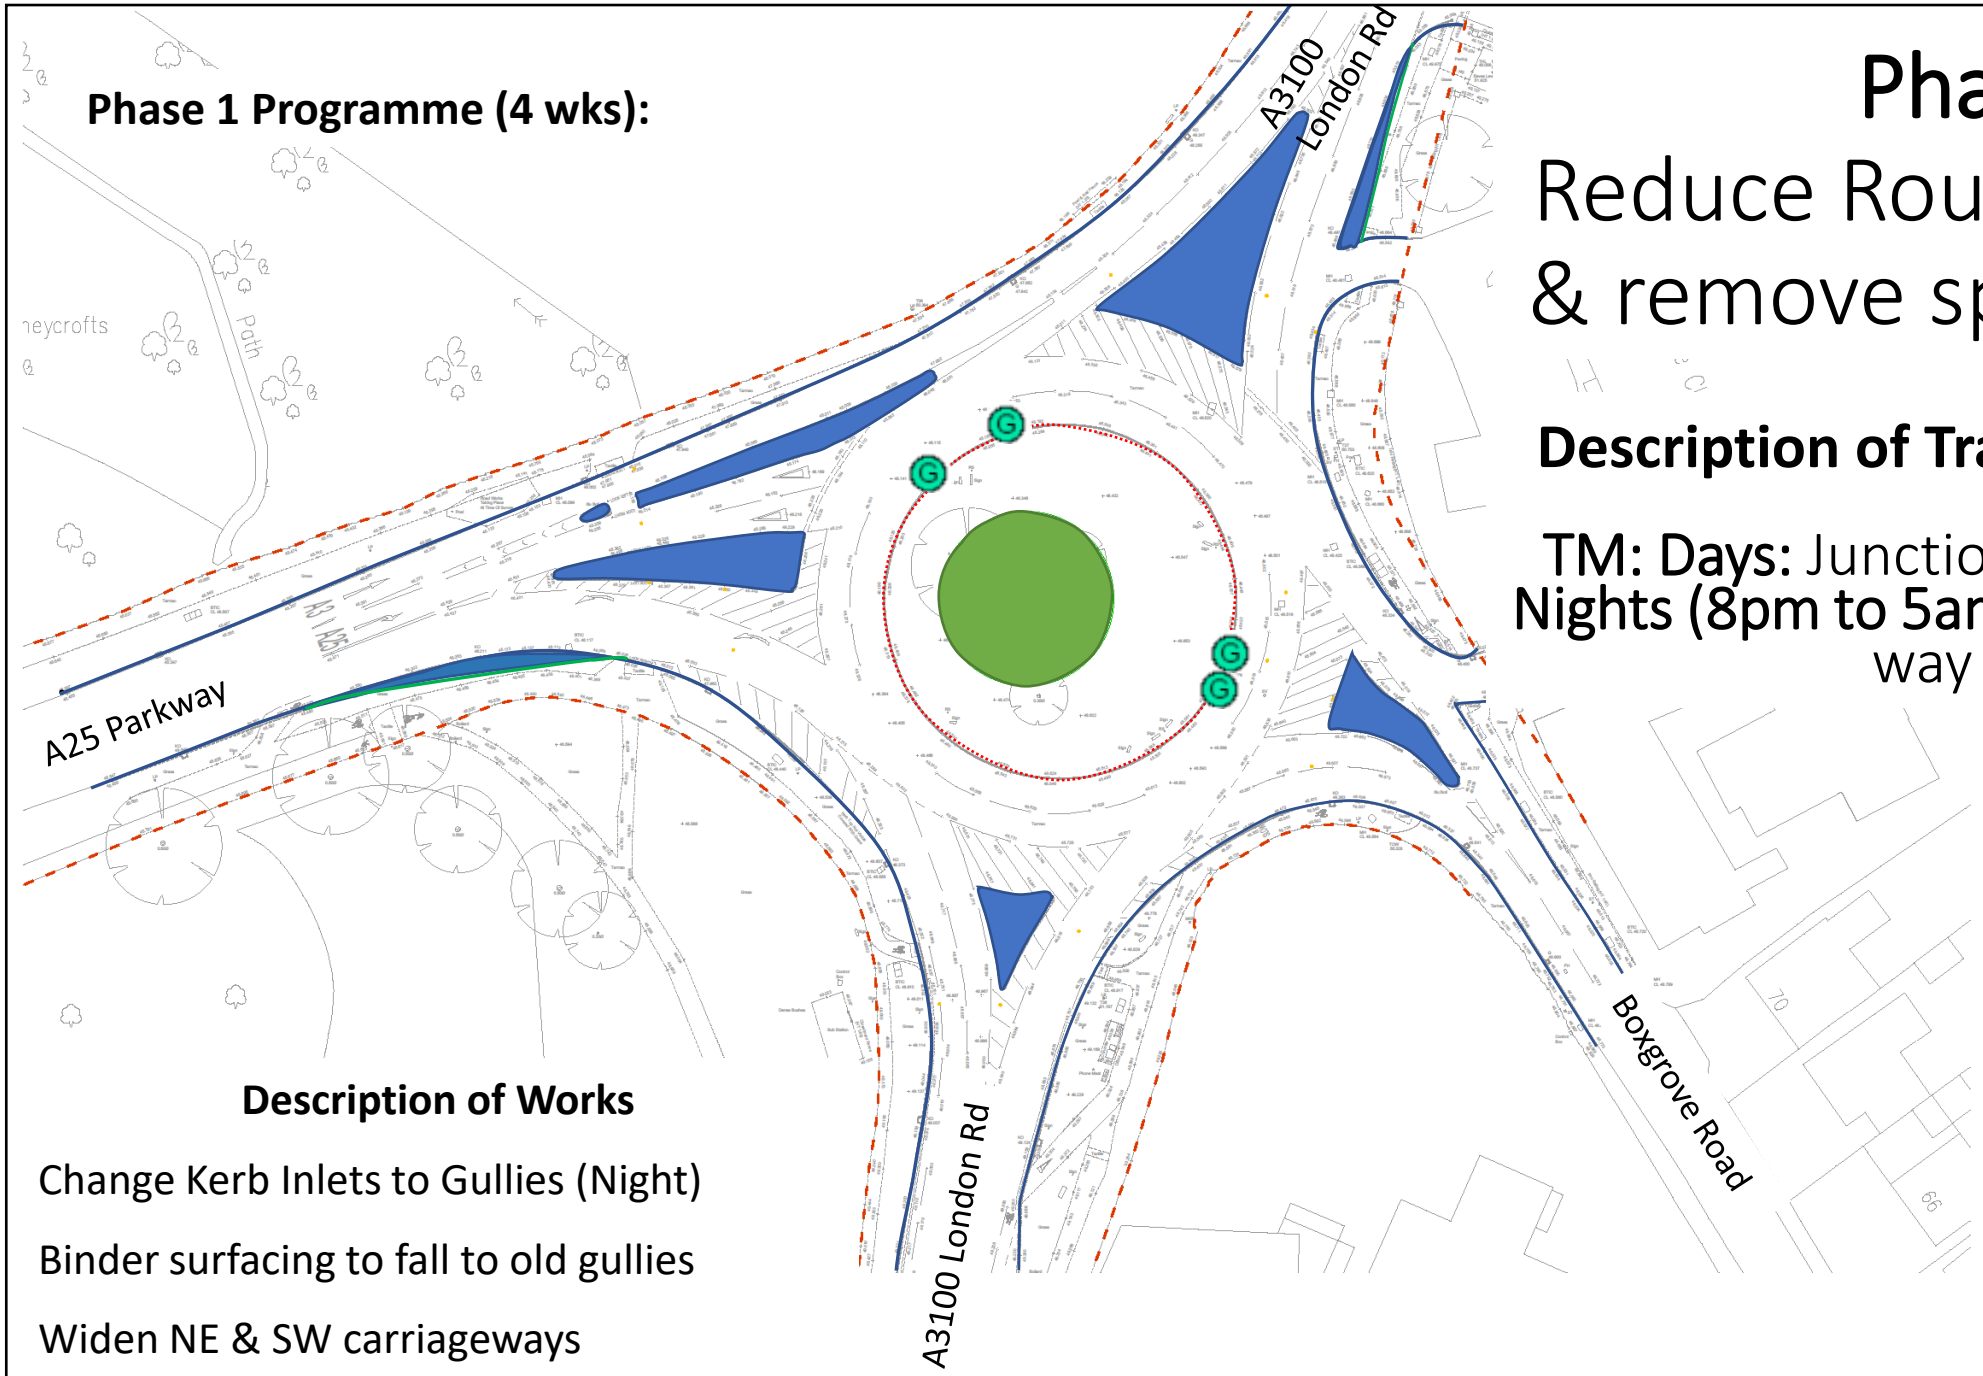

Phase 1

Reduce Roundabout size & remove splitter islands

Description of Traffic Management

TM: Days: Junction fully functioning
Nights (8pm to 5am): Lane closures/4-way lights

Description of Works


Change Kerb Inlets to Gullies (Night)

Binder surfacing to fall to old gullies

Widen NE & SW carriageways

Phase 2 Programme (3wks):

Phase 2
Construct 8x new Splitter Islands

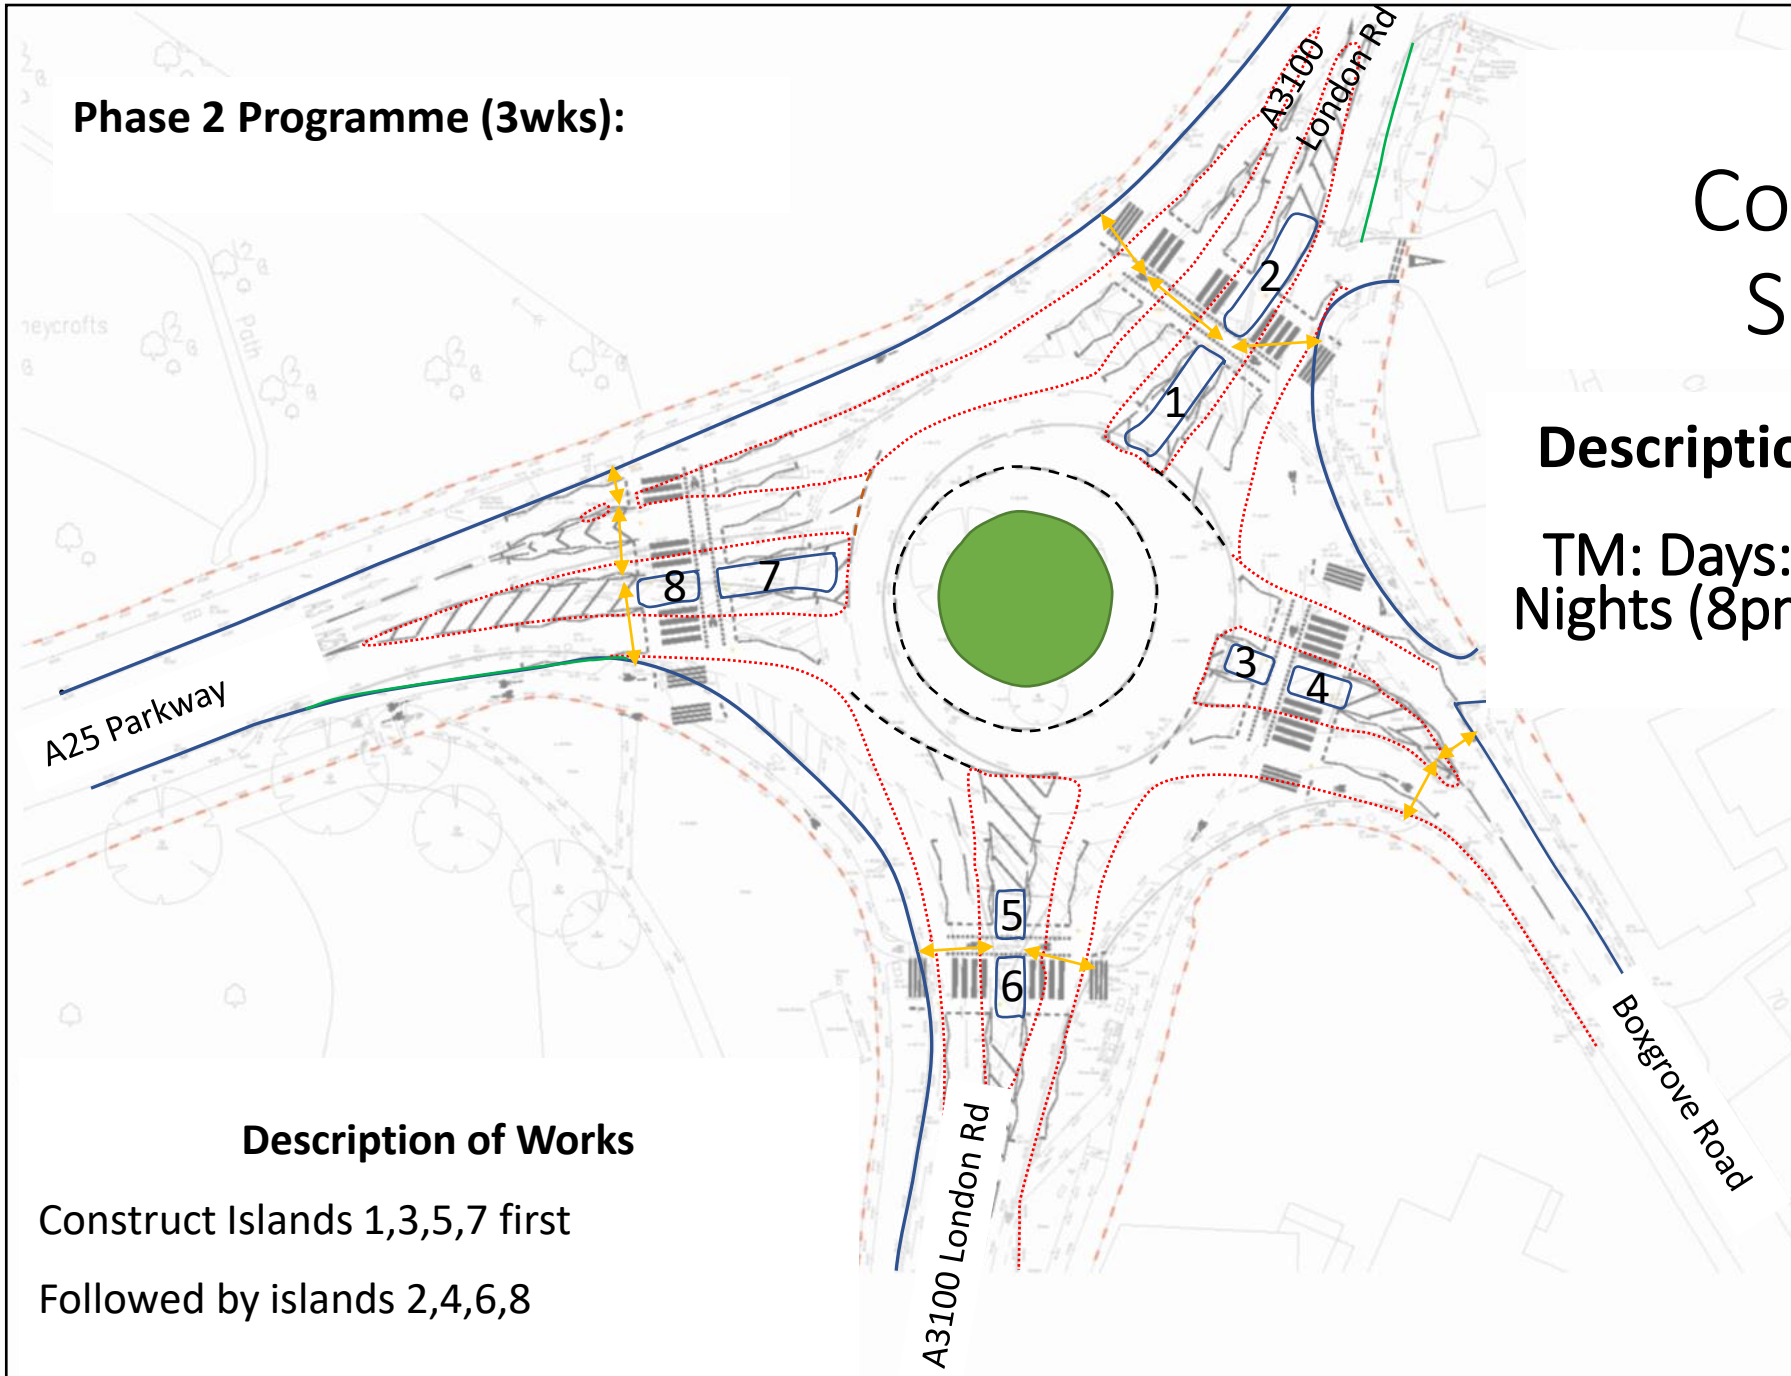

Description of Traffic Management


TM: Days: Junction fully functioning
Nights (8pm to 5am): Lane closures/4-way lights

Description of Works

Construct Islands 1,3,5,7 first

Followed by islands 2,4,6,8

Phase 3 Programme (6wks):

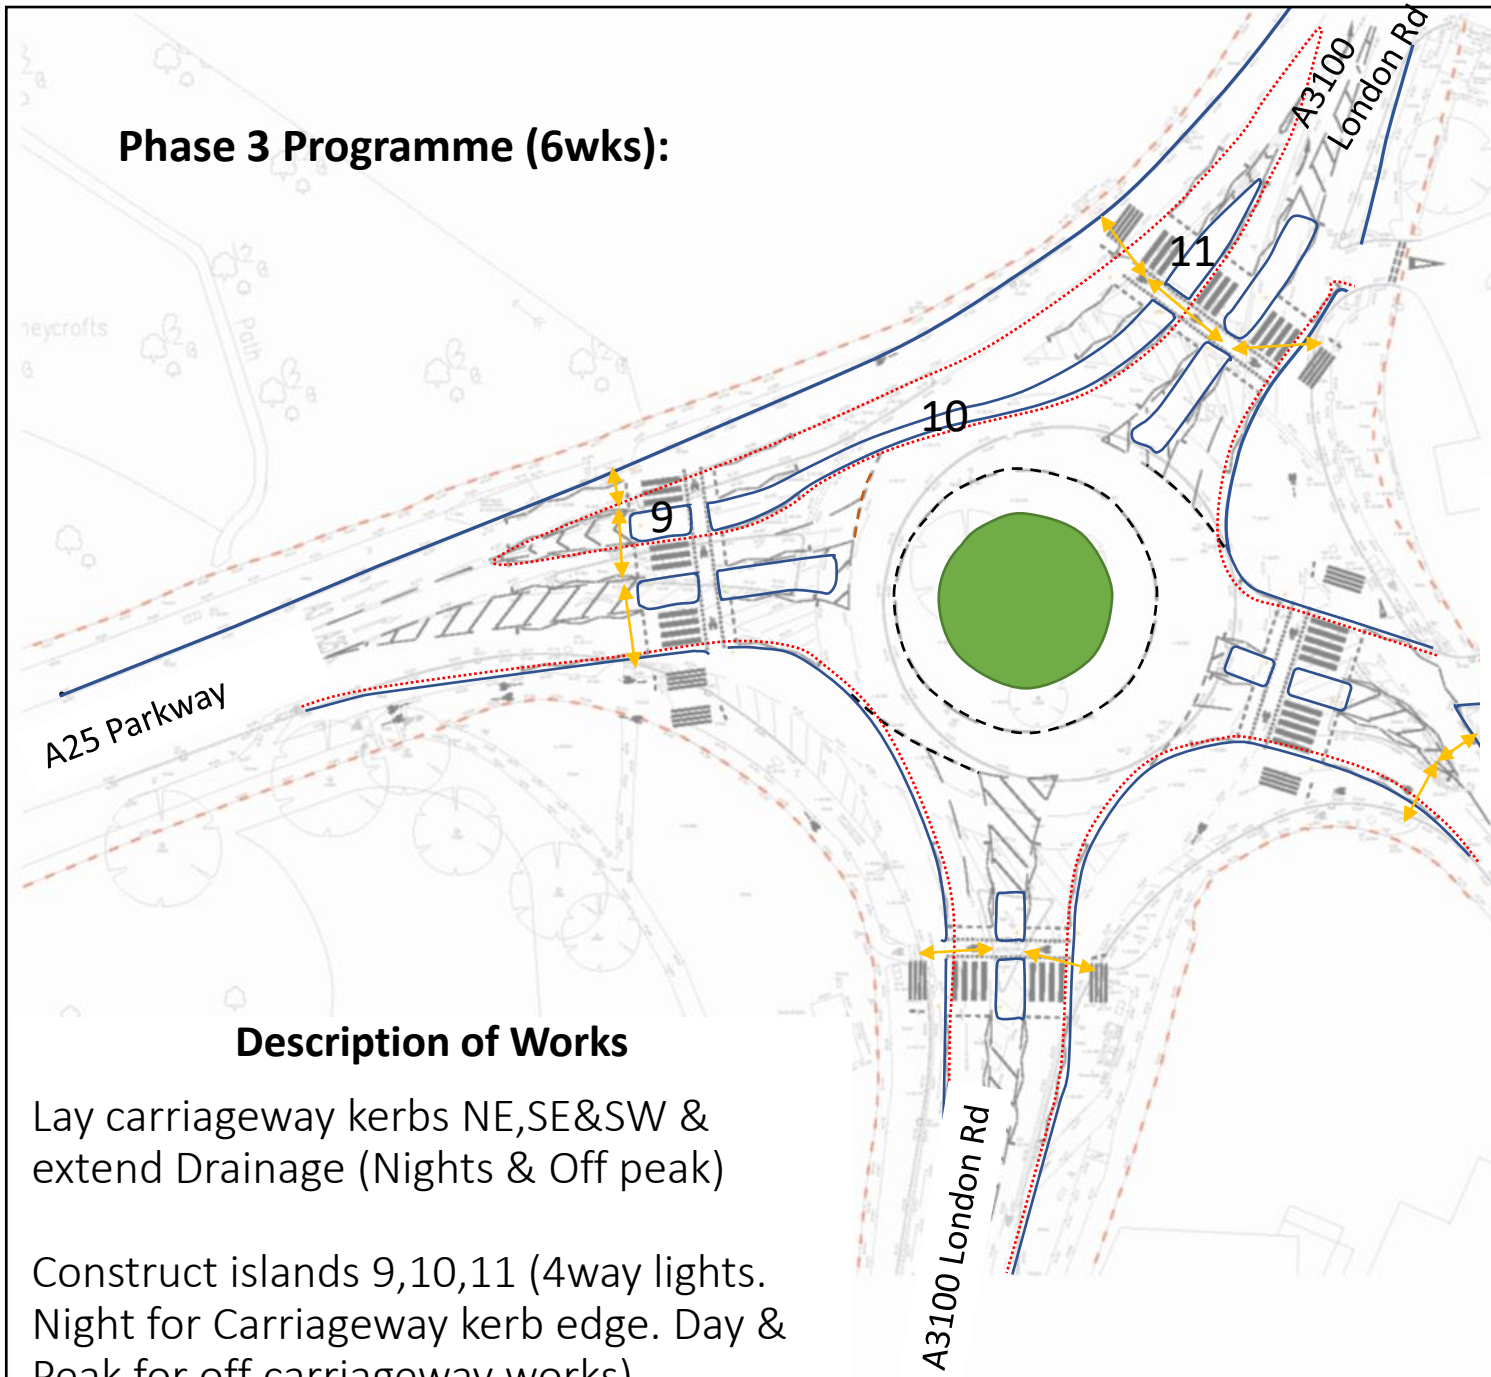

Phase 3

Build NE, SE, SW carriageway edge & 3x Islands

Description of Traffic Management


TM: Days: Junction fully functioning
Nights (8pm to 5am): Lane closures/4-way lights

Description of Works

Lay carriageway kerbs NE,SE&SW & extend Drainage (Nights & Off peak)

Construct islands 9,10,11 (4way lights. Night for Carriageway kerb edge. Day & Peak for off carriageway works)

Phase 4 Programme (8wks):

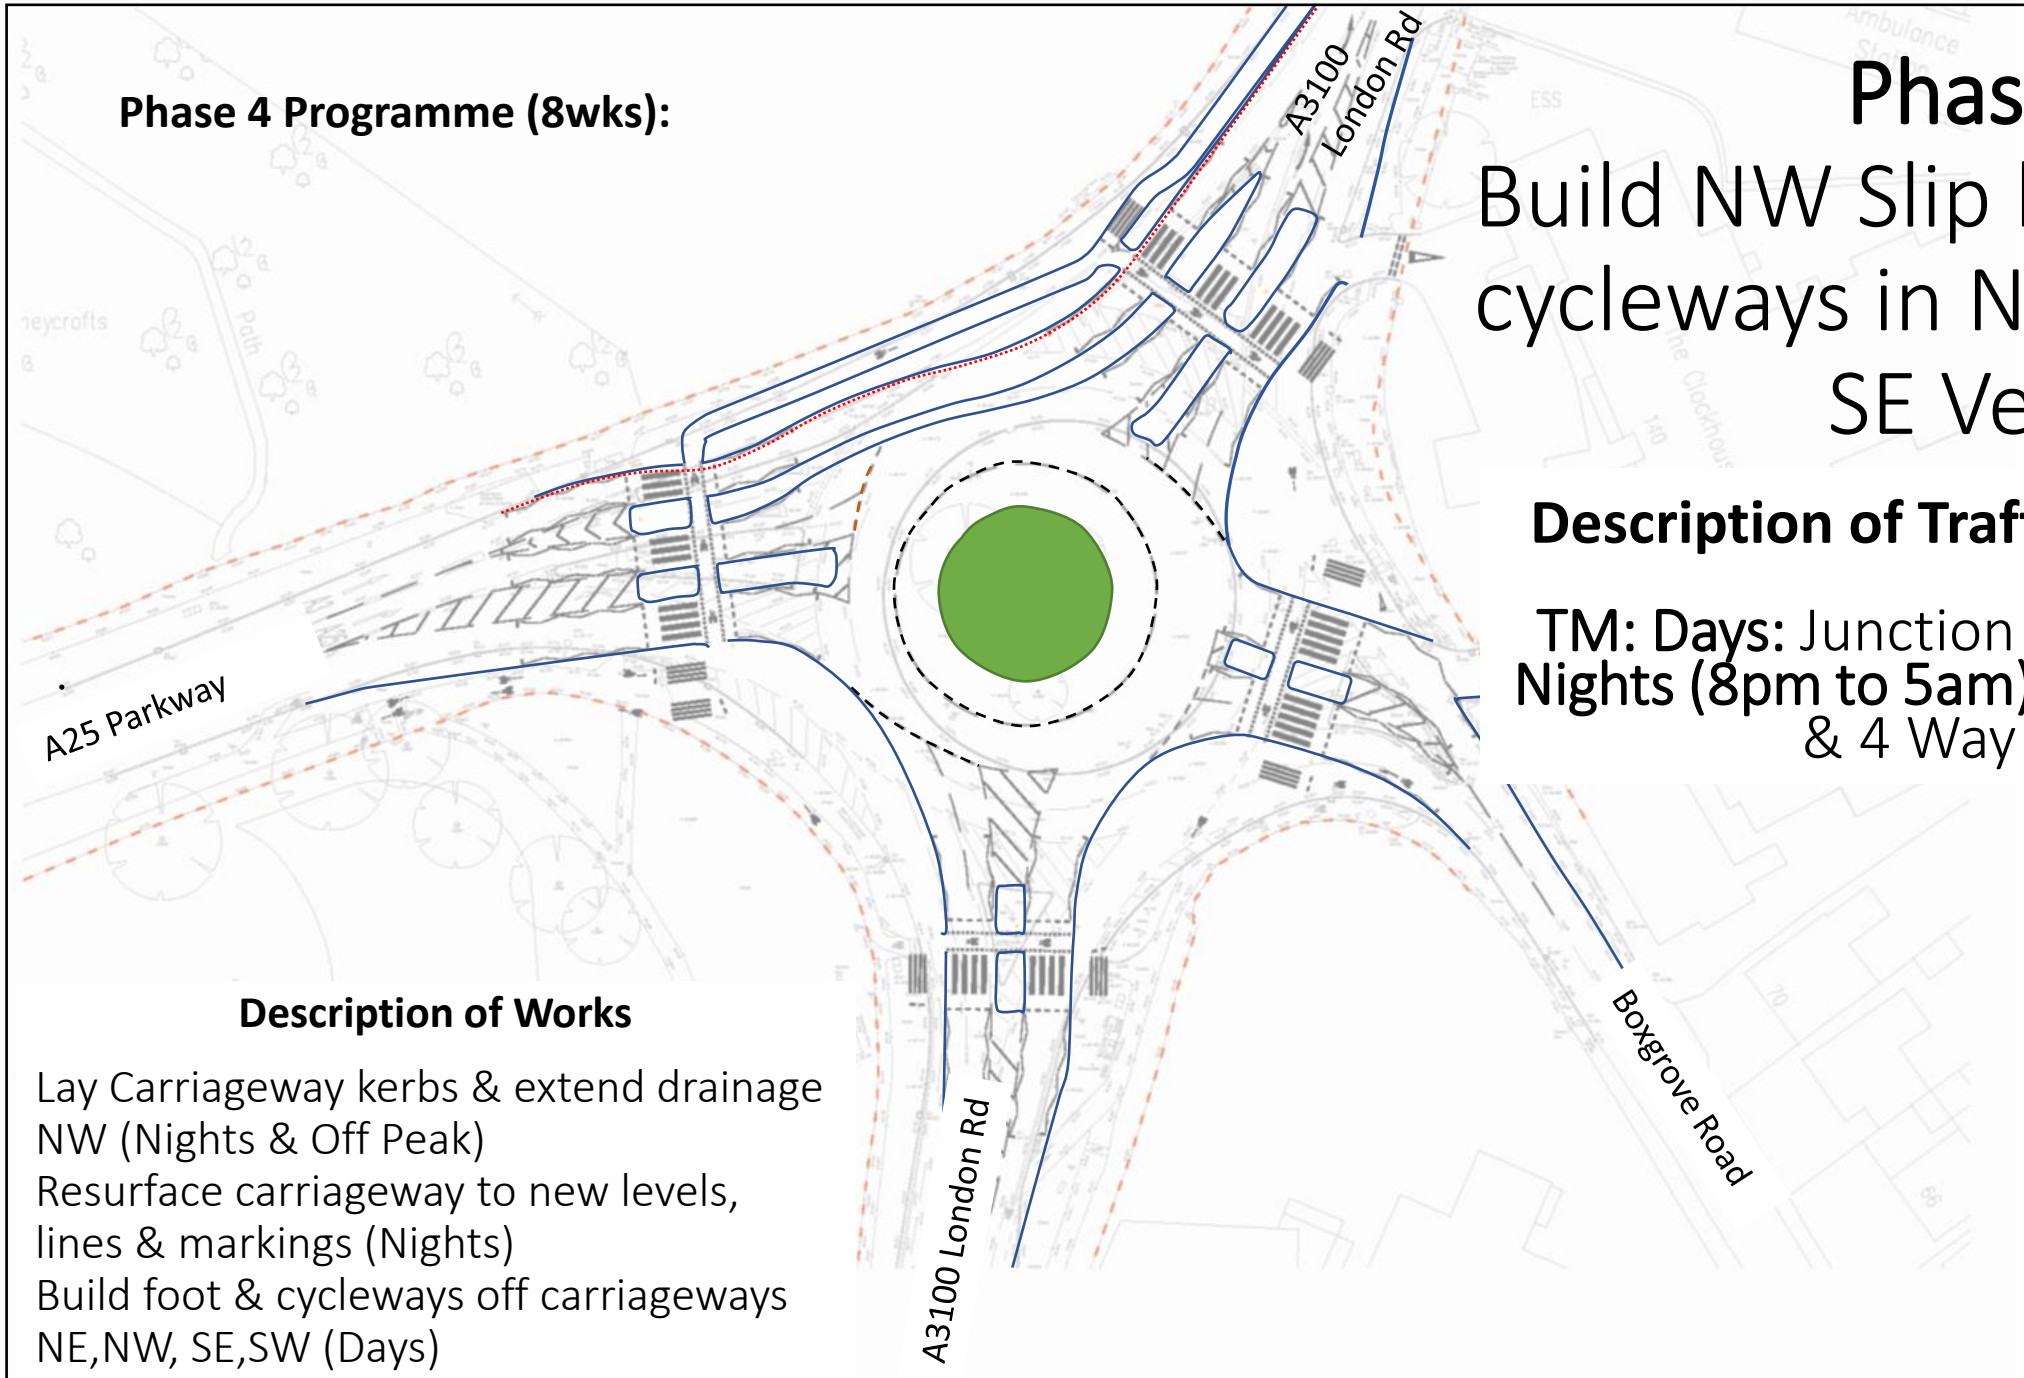

Phase 4

Build NW Slip lane, Foot- & cycleways in NE, NW, SW & SE Verge

Description of Traffic Management

TM: Days: Junction fully functioning
Nights (8pm to 5am): Slip Lane closed & 4 Way Lights

Description of Works

Lay Carriageway kerbs & extend drainage NW (Nights & Off Peak)
Resurface carriageway to new levels, lines & markings (Nights)
Build foot & cycleways off carriageways NE,NW, SE,SW (Days)

Works Completion

